


बृहन्मुंबई महानगरपालिका  
**MUNICIPAL CORPORATION OF GREATER MUMBAI**


(Sewerage Project Department)



**Chapter I) Hierarchy of Department**

Department of Chief Engineer (Sewerage Project)

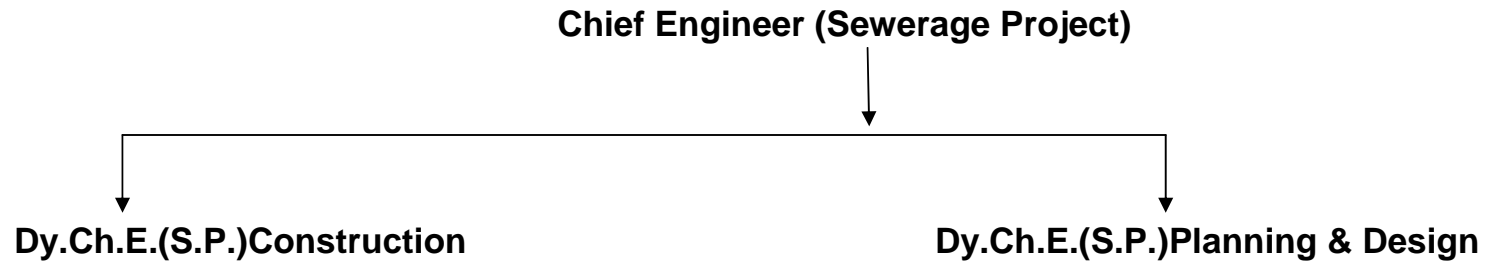


**Department of Dy.Ch.E.(S.P.)Construction Information**

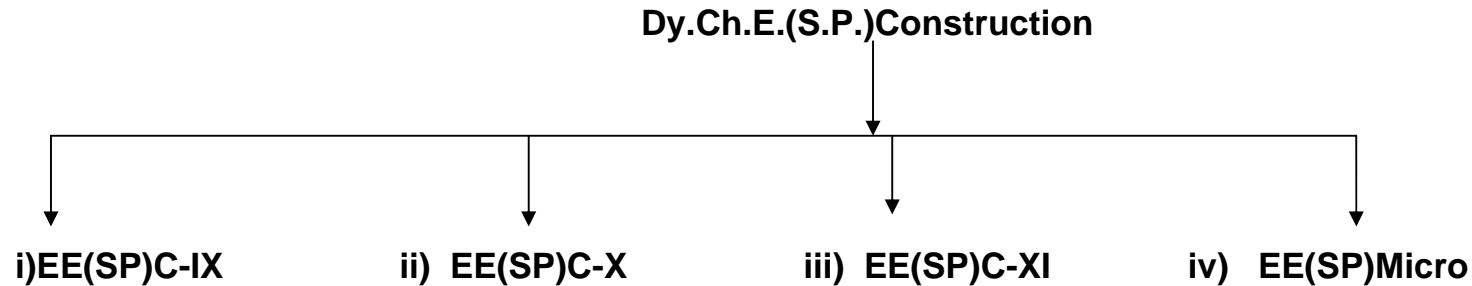


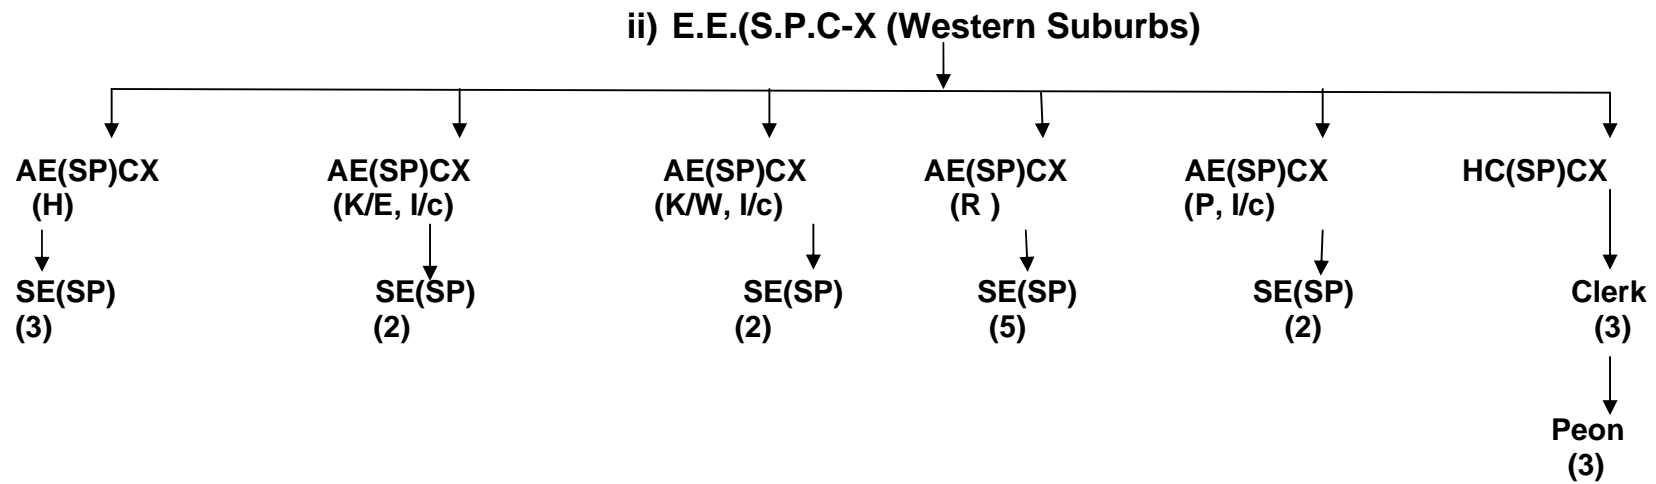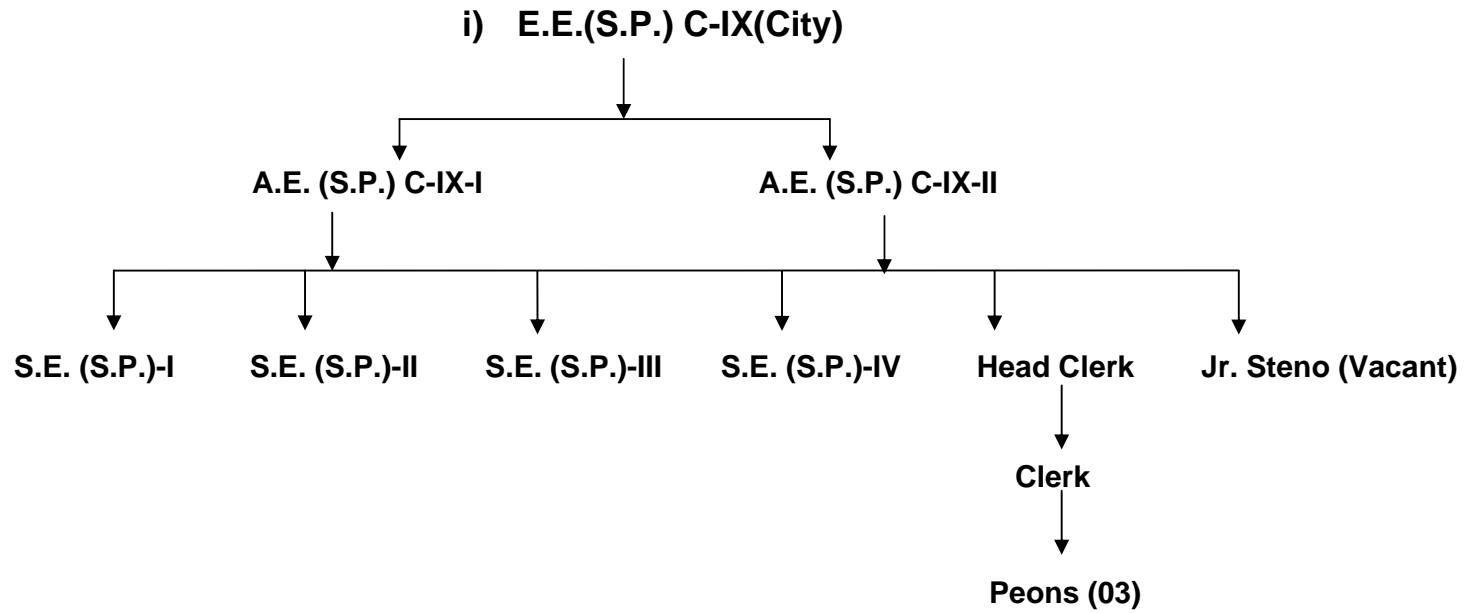

**iii) E.E.(S.P.C-XI (Eastern Suburbs)**

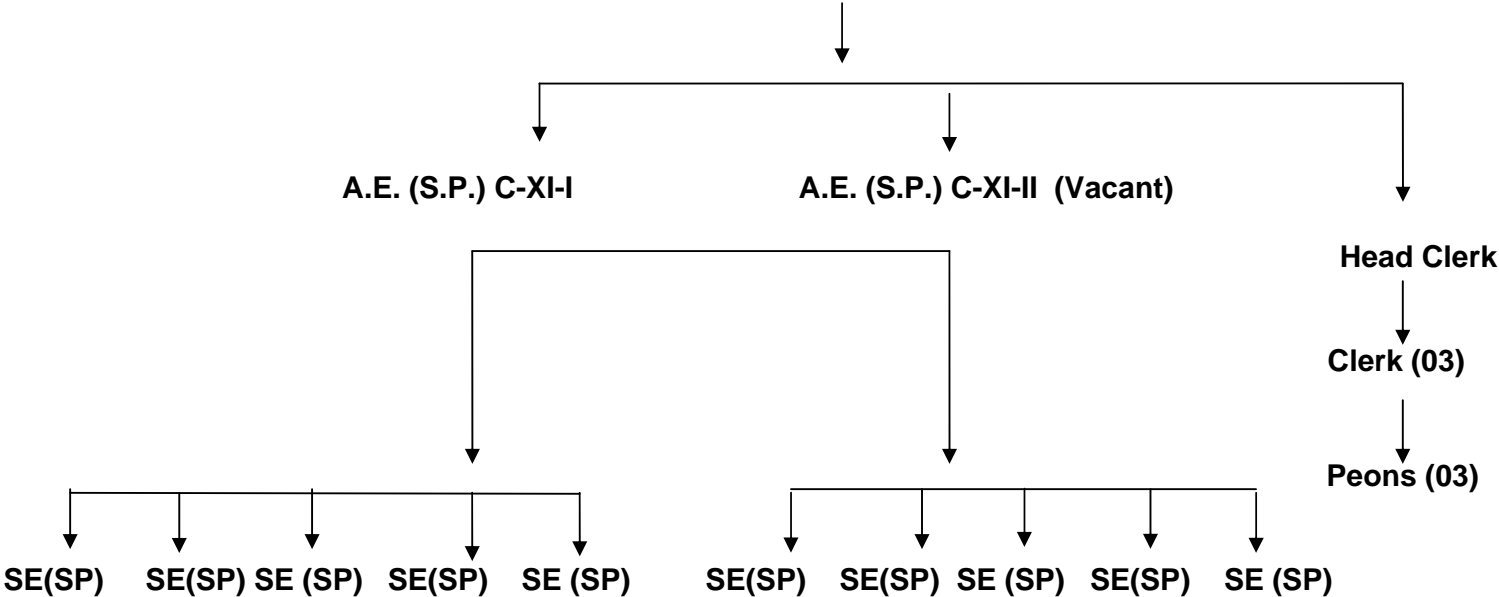

**iv) E.E. (S.P.) Microtunneling**

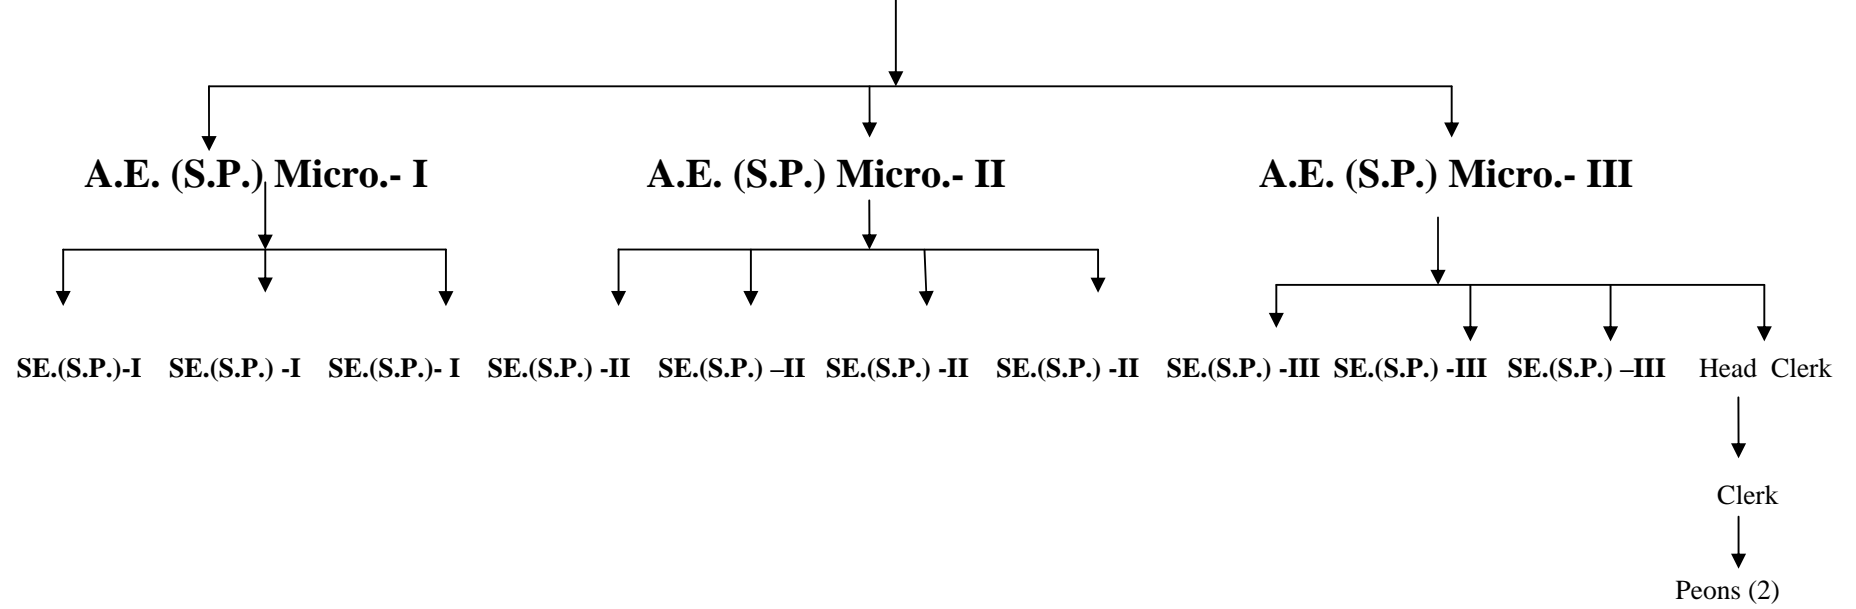

## Chapter II) Staff Information

### **i) E.E.(S.P.) Construction -IX(City)**

<b>Sr. No.</b>	<b>Name of Employee</b>	<b>Designation</b>	<b>E mail id</b>	<b>Phone No.</b>
1	Shri A.L.Mistry	E.E.(SP) C-IX	eeconstructioncity.sp @ mcgm.gov.in	<b>02224397886</b>
2	Shri.S.B.Shinde	AE(SP)C-IX-I	<b>eespconstructioncity @ gmail.com</b>	
3	Shri.Y.M. Killedar	AE(SP)C-IX-II		
4	Smt. S. P. Ranbhor	SE(SP)C-IX		
5	Shri. V.S.Salve	SE(SP)C-IX		
6	Shri. N.B.Torane	SE(SP)C-IX		
7	Shri.P.R. Pednekar	SE(SP)C-IX		
8	Smt.M.M.Samant	H.C.(SP)C-IX		
9	Smt.S.D.Chavan	Clerk		
10	Smt.V.S.Khairmode	Peon		
11	Shri.S.G.Ghare	Peon		
12	Shri.D.M.Morye	Peon		

**ii) E.E.(S.P.C-X (Western Suburbs))**

<b>Sr.No</b>	<b>Employee Name</b>	<b>Designation</b>	<b>Email ID</b>	<b>Phone No.</b>
1.	Shri A.L. Kate	E.E.(S.P.) C-X	eespcx@gmail.com	022 26125880
2.	Shri M.S. Jare	Asstt. Engineer (H)		
3.	Shri A. R. Sankhe	Asstt. Engineer (R)		
4.	Shri J.S. Thakar	Asstt. Engineer (K/E, I/c)		
5.	Shri A.G. Phatak	Asstt. Engineer (P, I/c)		
6.	Shri. S. J. Sawant	Asstt. Engineer (K/W, I/c)		
7.	Shri. Laxman P. Thore	Sub Engineer		
8.	Shri P.G. Gadekar	Sub Engineer		
9.	Shri S.D. Acharekar	Sub Engineer		
10.	Shri R. D. Karanjkar	Sub Engineer		
11.	Shri S.R. Dixit	Sub Engineer		
12.	Shri S.S. Gund	Sub Engineer		
13.	Shri Jamal S. Akhtar	Sub Engineer		
14.	Shri H.G. Mhadgut	Sub Engineer		
15.	Shri S.G. Dhanawade	Sub Engineer		
16.	Shri V.H. Jadhav	Sub Engineer		
17.	Shri. Abhishek Patil	Sub Engineer		
18.	Shri. Pradeep Jangam	Sub Engineer		
19.	Shri. S. Dorugade	Sub Engineer		
20.	Shri. Satish Mane	Sub Engineer		
21.	Shri. A. Upadhyay	Head Clerk		
22.	Shri K.D. Tribhuvan	Clerk		
23.	Shri Durgesh Mohkar	Clerk		

24.	Smt. Ujjwala Gharpure	Clerk		
25.	Shri G.K. Mirjolkar	Peon		
26.	Smt. Shweta Patankar	Peon		
27.	Shri S.J. Gosavi	Peon		

**iii) E.E.(S.P.)C-XI (Eastern Suburbs)**

Sr. No.	Name	Designation	E mail id	Phone No.
1	Shri. S.T.Sonawane	Ex.Eng.	<a href="mailto:eespcxi@gmail.com">eespcxi@gmail.com</a>	-----
2	Smt. N.S.Badwaik	Asst. Eng. I		
3	Shri. G.Y.Sane	Sub.Eng.		
4	Shri. N.D.Shikalgar	Sub.Eng.		
5	Shri. P.P.More	Sub.Eng.		
6	Shri. S.P.Tarkar	Sub.Eng.		
7	Smt. S.M. Deshmukh	Sub.Eng.		
8	Shri. N.G.Sonar	Sub.Eng.		
9	Shri. S.G.Khadapkar	Sub.Eng.		
10	Shri. S.J.Bhosale	Sub.Eng.		
11	Shri. D.P.Patil	Sub.Eng.		
12	Shri. A.K.Birari	Sub.Eng.		
13	Smt. S.R.Niphadkar	Head Clerk		
14	Shri. D.S.Mistry	Clerk		
15	Smt. Shalaka V.Hotkar	Clerk		
16	Smt. P.A.Patil	Clerk		
17	Smt. P.P.Shirke	Peon		
18	Shri. W.T.Dhage	Peon		
19	Shri. A.F.Shaikh	Peon		
20	Shri. P.R.Jankar	Peon		



**iv) E.E.(S.P.)Micro**

<b>Sr. No</b>	<b>Name</b>	<b>Designation</b>	<b>E-Mail</b>	<b>Phone No.</b>
1	Shri. Vishnu P. Vidhate	Executive Engineer (Sewerage Project) Micro	<b>eesp.micro1@g mail.com</b>	<b>022- 24958001/2495810 1</b>
2	Shri. Ajit H. Kulkarni	Assistant Engineer (S. P.) Micro-I	<b>eesp.micro1@g mail.com</b>	<b>022-24075998</b>
3	Shri. Shrikrishna G. Ware	Assistant Engineer (S. P.) Micro-II		
4	Shri. Pradeep M. Kulkarni	Assistant Engineer (S. P.) Micro-III		
5	Shri. Imtiaz Ahmad Ansari	Sub Engineer		
6	Shri. Subhash B. Shirsat	Sub Engineer		
7	Shri. Anil V. Harne	Sub Engineer		
8	Shri. Anil S. Varade	Sub Engineer		
9	Shri. Baban T. Potre	Sub Engineer		
10	Shri. Bharat Ramdas Saindane	Sub Engineer		
11	Shri. Shashikant S. Shinde	Sub Engineer		
12	Smt. Priyanka Jagadish Pethkar	Sub Engineer		
13	Shri. Ganesh B. Kadam	Sub Engineer		
14	Shri. Vijay S. Pimpaldohkar	Sub Engineer		
15	Smt. Vrinda Vinod Gadre	Head Clerk		
16	Shri. Rajesh Vilas Wagh	Clerk		
17	Shri. Mahendra S. Sasane	Peon		
18	Shri. Devraj Basana	Peon		

## **Chapter III) Office Addresses**

### **i) EE(SP)CIX(City)**

**Office of the Executive Engineer  
(Sewerage Project) C-IX  
327, G/North Ward Office Building,  
Harishchandra Yelve Marg,  
Dadar (West),  
Mumbai – 400 028.  
Phone No.-02224397886**

### **ii) EE(SP)C-X(W.S.)**

**Office of the,  
Executive Engineer (Sewerage Project)  
Construction-X, Annasaheb Vartak  
Market Building, 1<sup>st</sup> floor,  
Vallabhbai Road, Vile Parle (W),  
Mumbai 400 056.  
Phone No.: 2612 58 80**

**iii) EE(SP)C-X(E.S.)**

**Office of the Executive Engineer  
(Sewerage Project) C-XI  
4th floor ,District Center,  
CTS No. 1196/B ,Kanjur Village ,Near Parivar Society,  
Kanjur Marg(East)  
Mumbai – 400 042.**

**iv) EE(SP)Micro**

**Office of the Executive Engineer,  
(Sewerage Project) Microtunneling,  
Engineering Hub Building,  
2<sup>nd</sup> floor, Dr. E. Moses Road,  
Worli, Mumbai – 400 018.  
Tel. No. : 24958001/ 24958101/ 2407 5998.**

## Chapter IV) Ongoing Works under Construction Wing

i) ONGOING OPEN CUT WORKS UNDER EE(SP) C - IX as on 31.12.2015

Sr. No.	G.L Code	Name of the Work	Contract Cost	Contract Period (In Months)  Date of Starting  Date of Completion	Budget Estimate 2015-16	Cumulative Expenditure upto 31.12.2015	% of Actual Exp. With BE 2015-16	Remarks
1	2	3	4	5	6	7	8	9
1	505200276	P/L RCNP3 Class Pipe sewer along Sant Rohidas Marg & Sion-Bandra Road (from ONGC junction to 60' Road junction) Dharavi, G/North Ward.	2.08	9 (E.M) <u>31/03/14</u> <u>02/11/15</u>	1.00	0.68	68.31	As per new guide line for extra / excess, work is proposed to be forclosed.
2	505200327	P/L 300,350,450 mm dia RCNP3 class pipe sewer in place of 230mm dia S.W. pipe sewer along V.B. Worlikar Marg, Worli Koliwada in 'G/South' ward.	2.23	6 (EM)	2.00	0	0.00	Work is in Progress.
		<b>TOTAL</b>			<b>3.00</b>	<b>0.68</b>	<b>22.77%</b>	

ia) ONGOING MICROTUNNELLING WORKS UNDER EE(SP) C - IX as on 31.12.2015

(Rs. in Crore)

Sr. No.	G.L Code	Name of the Work	Contract Cost	Contract Period (In Months) Date of Starting Date of Completion	Budget Estimate 2015-16	Cumulative Expenditure upto 31.12.2015	% of Actual Exp. With BE 2015-16	PRESENT STATUS
1	2	3	4	5	6	7	8	9
1	505200289	<b>Package - 3</b> P/L 1200 mm dia gravity sewer line by Microtunnelling and pipe jacking method from Sion Koliwada Pumping Station to Duncan Causeway work.	30.38	23 01.10.2014 30.04.2017	5.00	0	0.00	Work is in progress
2	505200294	<b>Package - 5</b> Upsizing of existing sewer line by providing 600 mm dia sewer line from Kale road to premier road, by trenchless technology at Kurla (West), in 'L' ward.	13.37	12 01.01.2016 30.04.2017	2.00	0	0.00	Work will be started on 01/1/2016 as per phase programme.
3	505200296	<b>Package - 7</b> Upsizing of existing sewer line on L.B.S. marg from Netaji Palkar road to Vidyavihar station road, Vidyavihar (West), in 'L' ward.	3.93	19 01.01.2016 17.02.2018	3.00	1.69	56.33	work is in progress. During the month of Dec. 2015, 120 RM length of Pipe has been laid.

4	505200297	<b>Package - 6</b> Upsizing of existing sewer line by laying 1200 / 1600 mm dia sewer by microtunnelling and pipe jacking method on L.B.S. marg from M.N. road Junction to Surve chowk to Kurla Pumping station, Kurla (W) in 'L' ward.	31.01	11 01.01.2017 17.02.2018	2.00	0	0.00	Work will be started from 01.01.2017 as per phase programme.
5	505200318	<b>Package - 2</b> P/L 800 mm dia R.C.(NP3 Class) carrier pipe sewer through 1200mm dia RCC (NP 4 and above) sleeve pipe by micro-tunneling and pipe jacking method for Railway Crossing at Sewree railway station in Sewree Koliwada F/South Ward.	2.65	7 01.05.2017 17.02.2018	0.50	0	0.00	Work will be started from.01/5/2017 as per phase programme.
6	505200319	<b>Package - 9</b> P/L 800mm dia R.C.(NP3 Class) carrier pipe sewer through 1200mm dia R.C.C. (NP-4 and above) sleeve pipe by micro-tunneling method and pipe jacking method from Powai Pumping Station to existing 800mm dia sewer near Gandhi Nagar along Adishankaracharya Marg which is connected at L.B.S. Junction in 'S' Ward.	32.61	23 01.10.2014 30.04.2017	5.00	0	0.00	work is in progress

7	505200006	<b>Package - 1</b> P/L sewer in different locality in City area. 1. P/L sewer along Mahadev Palav Marg 2. P/L sewer at Abhilasha Nagar3. P/L 350 mm dia R.C.(NP3 Class) pipe sewerline through 1200 mm dia R.C.Pipe Carrier by microtunneling and pipe jacking method for missing link SWD portion along Megazine Street, opp. Abhilasha Nagar at Ray Road in 'E' Ward.	1.60	11 01.10.2014 31.12.2015	1.50	0	0.00	work is in progress
8	505200229	<b>Package - 4</b> D) P/L 600mm dia R.C.pipe sewerlines by microtunneling method and pipe jacking method on Marwah Road Crossing Ashok Nagar Bridge on Mithi River, Kurla (W) in 'L' Ward.(SP/MICRO/21).	1.61	11 01.01.2017 17.02.2018	1.50	0	0	Work is in progress

9	505200314	<b>Package - 8</b> ii) P/L 1200mm dia R.C. pipe sewerlines by micro tunneling method and pipe jacking method at Eastern Express Highway, JVLR crossing & Nalla crossing near Kannamwar Nagar, Vikhroli (E) in 'S' Ward.	6.83	7 01.05.2017 17.02.2018	0.25	0	0	work will be started from 01.05.2017 as per phase programme.
		<b>TOTAL</b>			<b>20.750</b>	<b>1.69</b>	<b>8.14%</b>	



**ii) ONGOING WORKS UNDER E.E.(S.P.) C-X**

(Rs. in Thousand)

Sr.No.	G.L. Code	Description of the work (Name of the contractors)	Contract Cost	Time period	Budget Estimate (2015-16) (Rs.)	Cumulative upto 31.12. 2015	% of actual expenditure with BE 15-16	Present status
1	2	3	4	5	6	7	8	9
1	505200173	P/L 600 mm dia. 350 mm dia. R.C. NP3 Class sewer line from Lucky Hotel along Station Road along Slaughter Road, upto Badi Masjid House, Bandra (W), H/West Ward. (Partly by trenchless technology) <b>M/s. United Construction Co.</b>	77722	15 E.M.	24000	45435	58.46%	Work is in progress.
2	505200183	P/L 900 mm dia R.C.NP3 class pipe sewer from Millennium Club to Lallubhai Park Extension Road, Andheri (W) in K/West Ward. (Partly by Open Cut Method and partly by Trenches Technology (Micro tunneling)) <b>M/s. United Construction Co.</b>	130885	20 E.M.	15000	80627	61.60%	Work will be started after receipt of Traffic NOC..
3	505200268	P/L 800 mm dia. R.C. NP3 Class Pipe sewer from Subhash Road to Western Express Highway near Azgaonkar Plot, Jogeshwari (East) in K/E Ward. <b>M/s. United Construction Co.</b>	51577	30 E.M.	50000	13888	26.93%	Work is in progress.
4	505200269	a) P/L 300 mm dia & 450 mm dia RC NP3 class pipe sewer from Majas Depot to Matoshri Club along south side of proposed Service Road of J.V.L.R., Jogeshwari (East) in K/East Ward.	55034	30 E.M.	10000	6445	11.71%	Work is in progress.

		b) Remaining work for P/L 300 mm dia s.w. pipe sewer line along Marol-Maroshi Road through Marol Gaothan Village upto Green Court Building in K/East Ward, Andheri (E). <b>M/s. United Construction Co.</b>						Work is completed.
5	505200037	Remaining work for P/L 230 mm dia s.w. pipe sewer along the road from Behram Baug upto the ext. sewer line off. Veera Desai Road, Near Bus Depot, Andheri (West) in K/West Ward. <b>M/s. United Construction Co.</b>	1051	30 E.M.	1500	0	0.00%	Work is yet not started due to court litigation.
6	505200308	Providing & laying 600 mm. dia sewer from Shivsgar hotel-along Shradhanand Road up to service road of W.E. Highway, Vile-Parle (E) K/E Ward. <b>M/s Akash Engineering Consultant</b>	43243	18 E.M.	20000	9539	22.06%	Work is in progress.
7	505200113	Missing link work of P/L 230 mm dia S.W. pipe sewer line along Church Road, Bori Colony and P/L 350 mm dia (R.C. NP3 Class) pipe sewer line along Kadamwadi Road, Andheri (East) in K/East Ward (connectivity by HDD method approx.25 Rmt.) (MSDP-II/C-I/SP/AS/WS-6) <b>M/s. Akash Engineering Consultant</b>	10115	18 E.M.	8300	2050	20.27%	Work is in progress.
8	505200311	P/L 400 mm. dia, 350 mm. dia R.C. NP3 class pipe sewer line in S.V.P. Nagar (MHADA Layout), Andheri (West) in K/West Ward. <b>M/s. Manisha Construction Co.</b>	36970	11 E.M.	15000	6573	17.78%	Work is in progress.

9	505200278	P/L sewer line of 350 mm & 500 mm & 600 mm dia R.C. NP3 Class sewer at 44 ft. wide D.P. Road from Thakur Complex circle to Junction of 90 ft. wide D.P. Road at Thakur Complex, Kandivali (E) in R/South Ward. <b>M/s. Narendra Construction</b>	65060	19 E.M.	25000	33483	51.46%	Work is in progress.
10	505200008	P/L 350 mm dia R.C. (NP3 class) pipe sewer along Suhasini Pawaskar Road and along D.P. Road in Vaishali Nagar at Dahisar (East) in R/North Ward. <b>M/s. United Construction Co.</b>	29809	17 E.M.+3.5 M. (T.E.)	3500	18900	63.40%	Work is completed.
11	505200302	P/L 1200 mm dia RC NP3 class pipe sewer from the junction of Turel Pakhadi Road and Liberty Garden Road No.2 to Link Road, Malad (West) in P/North Ward. <b>M/s. Yogesh Constructions Pvt. Ltd.</b>	64071	16 E.M.	28000	16718	26.09%	Work is in progress.
12	505200303	P/L sewer line of 400 mm dia RC NP3 class sewer at 60 ft. wide D.P. Road from Dattani Park Road to 120 ft. wide D.P. Road at Thakur Village, Kandivali (East) in R/South Ward.	58360	8 E.M.	32500	11561	19.81%	Work is in progress.
13	505200358	i) P/L 250 mm dia R.C. NP3 class pipe sewer line from three different roads i.e. road no.1, 2 & 4 at Lokhandwala road, Kandivali (East) in R/South Ward.	8400	5 E.M.	3400	2786	33.17%	Work is in progress.

14	505200344	ii) P/L 500 mm dia R.C. NP3 class pipe & 230 mm dia R.C. NP3 class pipe sewer in Shastri Nagar Road No.2, Goregaon (W) in P/South Ward. <b>M/s. D.B. Infratech</b>	26601		12000	2870	10.79%	Work is in progress.
15	505200307	Providing & laying 600 mm dia RC NP3 class sewer on existing road from Yari Road Masjid to Godgift tower, Versova, Andheri (W) K/West ward. <b>M/s Akash Engineering Consultant</b>	10085	18 E.M.	3085	4872	48.31%	Work will be started after receipt of Traffic NOC..

ii) Ongoing works under EE(SP)C-XI

**(Rs. in Crore)**

Sr. No.	GL Code	Name of Work	Contract Cost (In crore)	Time Period	Budget Amount(In crore)		Expenditure from 1.4.2015 to 31.12.2015 (In crore)	Percentage Comp. with RE 2015-16	Remarks
					BE 2015-16	RE 2015-16			
1	50520019 1	P/L 1000,600,400,300 mm dia. sewer line along 27.45m wide D.P.Road, existing kaccha road,internal roads at Cheeta camp & Trombay village road,M/E Ward. M/s RPS Infraprojects Pvt.Ltd.	26.17	32 E.M.	6	3.5	0	0	At present approval from Divisional Engineer (LM) ,CSTM ,Central Railway is obtained for design and drawing for the work in Railway premises.The amount of Rs.5,66,35,916/- has been deposited to Railway towards the way leave charges ,civil charges ,deposit charges & service tax etc .The approval from commissioner of Railway Safety (CRS) is awaited.It is proposed to delete the part of 190m sewer line as it requires to oprate extra items to the extent o 22.32% and same is not permissible as per new guidelines for Extra/excess items u/no. Dir./ES&P/324 dated 15/7/2015.

2	50520028 1	Part I (a) 800mm dia RCNP3 class pipe sewer from Sakinaka pumping station to the south side of compound wall of cemetery a plot along Sagbaug Road in K/East ward Andheri East (by open cut method). M/s. Valsons	16.66	14 E.M.	4	4	0	0	Work is in progress .
		Part II P/L 700mm dia RCNP3 pipe sewer along west bank of mithi river from Laffarge India company to junction of military road near Ashok Nagar bridge in Andheri East K/East ward (by open cut method) M /s. RE Infra Pvt. Ltd.		15 E.M.					Work is in progress .
3	50520013 2	P/L pipe sewer along Ashok nagar Road off Saki Vihar Road in 'L' Ward, Kurla (W) M /s. RE Infra Pvt. Ltd.	2.18	8 E.M.	1	1	0	0	Work is in progress .

## iv ) Ongoing Work under EE(SP)Micro

(Rs. in Crore)

Budget t Sr.No	GI.Code	Name Of Work	Contract t Cost (in crore)	Time Period	Budget Amount		Expenditur e from 1.4.2015 To 31.12.2015 (In crore)	Percentag e comp. with RE 2015-16	Remark
					BE 2015-16	RE 2015- 16			
18	50520023 7	<b>Package No.1</b> : P/L 1200mm dia. R.C. pipe sewer by Microtunneling and pipe jacking method along R.C. marg from Vashi Naka to L.U. Gadakari marg Jn. Chembur, M/W ward.	36.4621	16 1.10.2010 31.12.2015	5.0000	10.0000	4.99	49.9000	Micro Tunneling Drive Complete d
20	50520024 0	<b>Package No.4</b> : P/L 1000mm dia R.C. pipe for missing links of sewer line by Microtunneling and pipe jacking method along LBS marg between Tank road and Bhandup Village road Jn. in 'S' Ward.	4.786	16 1.10.2015 31.5.2016	1.0000	1.0000	0.0000	0.0000	Traffic NOC not Recived
22	50520029 0	P/L 1200 mm dia upsized sewer from Malad Pumping Station to Malvani Fire Brigade along Marve Road P/North and P/L 900 mm dia upsized sewer from Malvani Police Station to Malvani Fire Brigade,	25.2818	24 15.2.2015 31.1.2018	2.0000	11.0000	0.8900	8.0909	Work In Progress.

		Malad (W) P/North ward <b>(by Microtunneling).</b>							
25	50520029 3	a) Missing link on 1400 mm dia sewer line on Link Road by laying 1600 mm dia sewer line near Kalapradarshini Park at D N Nagar & P/L 1200 mm dia sewer line at junction of Link Road & J. P. Road, Andheri (W) in K/W ward (by Micro Tunneling) <b>(SP/MICRO/20)</b> b) P/L 1200 mm dia upsized sewer line from Apna Bazar to Link Road & J P Rd. junction, by microtunelling and pipe jacking method at Andheri west.	1.3514	24 15.2.2015 31.1.2018	<b>0.5000</b>	<b>0.9000</b>	0.0000	0.0000	Work in Progress.



101	50520026 8	P/L 800 mm dia RCNP3 class pipe sewer line from Subhash Road to Western Express Highway, Near Asgaonkar plot, Jogeshwari (E). <b>ANDP/L 600 mm dia pipe sewer from west of Western Express Highway to Majas Depot along southside of proposed service road of J.V.L.R., Jogeshwari (E).(by microtunneling)</b>	35.7148	241.3.2014 28.2.2017	<b>5.0000</b>	<b>16.0000</b>	4.6852	29.2825	Work in Progress
153	50520028 5	P/L RC pipe sewer line of 1800 mm dia along Link Road from Kandarpada junction to Vallabha Nagar pumping station, Dahisar in R/North ward in Mumbai by Microtunneling Method. <b>SP/MICRO/18</b>	51.29	24 1.3.2014 28.2.2017	<b>10.0000</b>	<b>33.7000</b>	9.7400	28.9021	Work in progress

162	50520028 2	P/L 750 mm dia sewerline at Akurli Road from East of Western Express Highway to Western Railway line <b>and</b> P/L 1200 mm dia sewerline from Western Railway line, Mathuradas Road to Link Road, Kandivali (W) (By trenchless method) <b>SP/MICRO/19</b>	88.7959	24 5.2.2014 31.12.2016	<b>10.0000</b>	<b>25.0000</b>	9.9700	39.8800	Work in progress
163	50520028 6	P/L RC pipe sewer line of 600 mm dia through 1200 mm dia carrier pipe for missing link along Dattani Park Road from existing MH no.8 to MH no.22, R/South ward, in Mumbai by Microtunneling Method. <b>SP/MICRO/18</b>	7.9061	24 1.3.2014 31.7.2015	<b>3.0000</b>	<b>4.8000</b>	2.8100	58.5417	Micro Tunneling Drive Completed

164	50520028 7	P/L RC 1200 mm dia pipe sewer line missing link along 90' DP Road, between existing scrapper MH no.0 near west side of W.E.Highway and MH no.2 near Sai Hospital, at Kandivali east, R/South ward in Mumbai by Microtunneling Method. <b>SP/MICRO/18</b>	1.1645	241.3.201431.1.2016	<b>0.8000</b>	<b>0.4000</b>	0.0000	0.0000	Traffic NOC Recently recived Excavatio n of pit / shaft Work in progress
231	50520001 2	Installation of sewer lines at various locations in Mumbai by Trenchless Technology (MSDP -II / C-I / SP/ US/ES1, ES3, ES4A, ES4B, ES5, ES6, ES7 & ES8C ) <b>SP/Micro/10</b>	99.2619	30 1.2.2008 31.12.2015	<b>3.0000</b>	<b>3.0000</b>	0.0000	0.0000	Work (R C Marg ) in progress
<b>Total</b>					<b>40.30</b>	<b>105.80</b>	<b>33.09</b>	<b>31.27</b>	
